



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd**Transformer (T1) Division**Smart solutions.
Strong relationships**Final Inspection****W.O.No :** : **ET10335****Serial No :** : **ET10335/1A****Customer :** : **ZETDC****JOB RATING :** : **3P2WDualHV****REFERENCE STANDARD :** : **IEC:60076****CUSTOMER REFERENCE :** : **-****SCHEDULE OF TESTS :** : **AS PER SHEET 3****TESTING DATE :** : **05/06/2015 To 05/06/2015****DATE OF ISSUE :** : **05/06/2015****TESTED BY****CHECKED BY****APPROVED BY****WITNESSED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 24/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**Voltage Class [kV]****Phase** : Three**Winding Designation** : HV LV**Terminal Notations** : 1U1,1V1,1W1,N 2U1,2V1,2W1,N**Rated Capacity [MVA]****ONAN** : 20 20**ONAF** : 30 30**Rated Voltage[kV]** : 132 - 88 11**Rated Current[A]** : 131.22 - 196.83 1574.64**Rated Frequency[Hz]** : 50**Connections** : STAR STAR**Vector Group** : YNyn0**Type Of Tap Changer** : OLTC & OLTC**% Voltage Variation On****OLTC** : Taps Provided On HV Winding For Variation Of HV Voltage From 7% To -7% in 1% Steps in 14 Steps**Transformer Type** : Power Transformer**OLTC** : Taps Provided On HV Winding For Variation Of HV Voltage From 10.5% To -10.5% in 1.5% Steps in 14 Steps**Temp. Rise. Of Oil/Wdg (°C)** : 60 / 65

INSULATION LEVELS	LINE TERMINALS	NEUTRAL TERMINALS
HV	LI (FW/CW) - 650/950kVp SI : 750kVp	LI - 325kVp
LV	LI (FW/CW) - 95/95kVp	N.A.

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 16/09/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**Tests Performed**

SRNO	TESTS	SHEET NO
1	MEASUREMENT OF VOLTAGE RATIO AND VECTOR GROUP VERIFICATION	4 - 6
2	MEASUREMENT OF WINDING RESISTANCE	7 - 8
3	MEASUREMENT OF INSULATION RESISTANCE OF WINDING	9
4	MEASUREMENT OF NO LOAD LOSS AND NO LOAD CURRENT	10
5	MEASUREMENT OF LOAD LOSS AND IMPEDANCE VOLTAGE	11 - 14
6	APPLIED VOLTAGE TEST	15
7	MAGNETIC BALANCE AND EXCITATION CURRENT TEST	16 - 17
8	MEASUREMENT OF POWER TAKEN BY COOLER CIRCUIT	18
9	OIL LEAKAGE TEST	19
10	MEASUREMENT OF ACOUSTIC NOISE LEVEL	20 - 21
11	LIGHTNING IMPULSE VOLTAGE WITHSTAND TEST	22 - 26
12	LIGHTNING IMPULSE VOLTAGE WITHSTAND TEST ON NEUTRAL TERMINAL	27
13	MEASUREMENT OF ZERO PHASE SEQUENCE IMPEDANCE	28
14	SWITCHING IMPULSE VOLTAGE WITHSTAND TEST	29
15	MEASUREMENT OF CAPACITANCE AND DISSIPATION FACTOR	30 - 31
16	INDUCED OVER VOLTAGE WITHSTAND TEST WITH PARTIAL DISCHARGE MEASUREMENT	32 - 33
17	CHECK OF CT RATIO AND POLARITY	34
18	SFRA MEASUREMENT	35 - 36
19	TEMPERATURE RISE TEST	37 - 46

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFIC

TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships

Date : 24/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

MEASUREMENT OF VOLTAGE RATIO

HV/LV(132/11kV)/1

TAP NO.	VOLTAGES (kV)		CAL. RATIO	MEASURED RATIO					
	HV	LV		1U1-N	%	1V1-N	%	1W1-N	%
				2U1-N	Error	2V1-N	Error	2W1-N	Error
1	141.2400	11.0000	12.8400	12.8410	0.008	12.8360	-0.031	12.8330	-0.055
2	139.9200	11.0000	12.7200	12.7110	-0.071	12.7130	-0.055	12.7120	-0.063
3	138.6000	11.0000	12.6000	12.6060	0.048	12.6080	0.063	12.6010	0.008
4	137.2800	11.0000	12.4800	12.4690	-0.088	12.4670	-0.104	12.4720	-0.064
5	135.9600	11.0000	12.3600	12.3690	0.073	12.3630	0.024	12.3600	0.000
6	134.6400	11.0000	12.2400	12.2360	-0.033	12.2360	-0.033	12.2300	-0.082
7	133.3200	11.0000	12.1200	12.1250	0.041	12.1280	0.066	12.1210	0.008
8(Nor)	132.0000	11.0000	12.0000	11.9980	-0.017	11.9960	-0.033	11.9980	-0.017
9	130.6800	11.0000	11.8800	11.8850	0.042	11.8900	0.084	11.8870	0.059
10	129.3600	11.0000	11.7600	11.7580	-0.017	11.7580	-0.017	11.7600	0.000
11	128.0400	11.0000	11.6400	11.6500	0.086	11.6500	0.086	11.6480	0.069
12	126.7200	11.0000	11.5200	11.5160	-0.035	11.5210	0.009	11.5200	0.000
13	125.4000	11.0000	11.4000	11.4110	0.096	11.4080	0.070	11.4100	0.088
14	124.0800	11.0000	11.2800	11.2920	0.106	11.2920	0.106	11.2940	0.124
15	122.7600	11.0000	11.1600	11.1810	0.188	11.1810	0.188	11.1820	0.197

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFIC

TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships

Date : 24/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

MEASUREMENT OF VOLTAGE RATIO

HV/LV(88/11kV)/2

TAP NO.	VOLTAGES (kV)		CAL. RATIO	MEASURED RATIO					
	HV	LV		1U1-N	%	1V1-N	%	1W1-N	%
				2U1-N	Error	2V1-N	Error	2W1-N	Error
1	97.2400	11.0000	8.8400	8.8350	-0.057	8.8330	-0.079	8.8350	-0.057
2	95.9200	11.0000	8.7200	8.7060	-0.161	8.7090	-0.126	8.7070	-0.149
3	94.6000	11.0000	8.6000	8.6000	0.000	8.5980	-0.023	8.5970	-0.035
4	93.2800	11.0000	8.4800	8.4700	-0.118	8.4690	-0.130	8.4780	-0.024
5	91.9600	11.0000	8.3600	8.3610	0.012	8.3610	0.012	8.3610	0.012
6	90.6400	11.0000	8.2400	8.2340	-0.073	8.2330	-0.085	8.2360	-0.049
7	89.3200	11.0000	8.1200	8.1120	-0.099	8.1230	0.037	8.1250	0.062
8(Nor)	88.0000	11.0000	8.0000	7.9950	-0.062	7.9960	-0.050	7.9950	-0.062
9	86.6800	11.0000	7.8800	7.8848	0.061	7.8840	0.051	7.8850	0.063
10	85.3600	11.0000	7.7600	7.7590	-0.013	7.7560	-0.052	7.7590	-0.013
11	84.0400	11.0000	7.6400	7.6470	0.092	7.6470	0.092	7.6470	0.092
12	82.7200	11.0000	7.5200	7.5200	0.000	7.5200	0.000	7.5190	-0.013
13	81.4000	11.0000	7.4000	7.4100	0.135	7.4090	0.122	7.4100	0.135
14	80.0800	11.0000	7.2800	7.2830	0.041	7.2810	0.014	7.2820	0.027
15	78.7600	11.0000	7.1600	7.1700	0.140	7.1690	0.126	7.1690	0.126

Results : All measured values are within ± 0.5 % tolerance of the specified values


WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

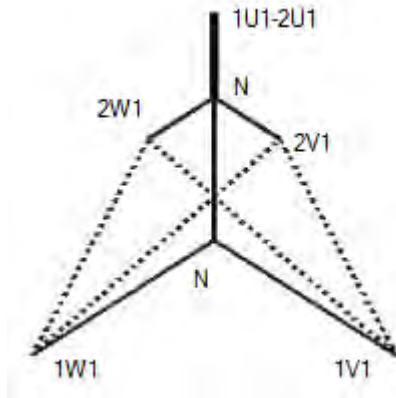The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 24/06/2015 **W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**VECTOR GROUP VERIFICATION****Shorted :** 1U1-2U1**3-Phase Supply :** 1U1-1V1-1W1

Measured		
1U1-1V1	429	Volts
1V1-1W1	428	Volts
1W1-1U1	435	Volts
1W1-2W1	389	Volts
1V1-2V1	393	Volts
1W1-2V1	406	Volts
1V1-2W1	409	Volts

(1W1-2W1) \approx (1V1-2V1)	389 \approx 393
(1W1-2V1) \approx (1V1-2W1)	406 \approx 409

Hence, Vector Group YNyn0 is confirmed.**WITNESSED BY****TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 16/07/2015 **W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**MEASUREMENT OF WINDING RESISTANCE****HV (88 kV) Winding Resistance in Ohms**

Top Oil Temp. : 42.6°C Bottom Oil Temp. : 39.8°C Avg. Oil Temp. : 41.2°C					
TAP NO.	1U1-N	1V1-N	1W1-N	Avg. Resistance @ 41.2°C	Total Resistance @ 75 °C
1	0.478940	0.479260	0.480180	0.479460	1.614402
2	0.469860	0.470160	0.471200	0.470407	1.583919
3	0.461800	0.462220	0.463100	0.462373	1.556868
4	0.452820	0.453180	0.454220	0.453407	1.526678
5	0.444680	0.445240	0.446140	0.445353	1.499559
6	0.434980	0.435460	0.436460	0.435633	1.466831
7	0.426840	0.427460	0.428320	0.427540	1.439581
8(Nor)	0.416180	0.415900	0.416060	0.416047	1.400882
9	0.426340	0.427080	0.427940	0.427120	1.438167
10	0.435680	0.436320	0.437260	0.436420	1.469481
11	0.443680	0.444420	0.445200	0.444433	1.496462
12	0.452980	0.453640	0.454580	0.453733	1.527776
13	0.460900	0.461780	0.462440	0.461707	1.554625
14	0.469500	0.470300	0.471000	0.470267	1.583448
15	0.477560	0.478380	0.478980	0.478307	1.610520

HV (132 kV) Winding Resistance in Ohms

Top Oil Temp. : 42.6°C Bottom Oil Temp. : 39.8°C Avg. Oil Temp. : 41.2°C					
TAP NO.	1U1-N	1V1-N	1W1-N	Avg. Resistance @ 41.2°C	Total Resistance @ 75 °C
1	1.105500	1.106300	1.106800	1.106200	3.724713
2	1.096100	1.096900	1.097500	1.096833	3.693174
3	1.087800	1.088600	1.089200	1.088533	3.665226
4	1.078400	1.079200	1.079900	1.079167	3.633690
5	1.070100	1.070900	1.071500	1.070833	3.605628
6	1.060000	1.060800	1.061500	1.060767	3.571734
7	1.051600	1.052400	1.053100	1.052367	3.543453
8(Nor)	1.040500	1.040500	1.040400	1.040467	3.503382
9	1.051100	1.052000	1.052700	1.051933	3.541989
10	1.060800	1.061600	1.062400	1.061600	3.574539
11	1.069100	1.070000	1.070600	1.069900	3.602487
12	1.078700	1.079600	1.080300	1.079533	3.634923
13	1.087000	1.088000	1.088600	1.087867	3.662985
14	1.095900	1.096900	1.097500	1.096767	3.692952
15	1.104300	1.105200	1.105700	1.105067	3.720900

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 16/07/2015 **W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**MEASUREMENT OF WINDING RESISTANCE****LV (11 kV) Winding Resistance in Ohms**

Top Oil Temp. : 42.6°C Bottom Oil Temp. : 39.8°C Avg. Oil Temp. : 41.2°C					
TAP NO.	2U1-N	2V1-N	2W1-N	Avg. Resistance @ 41.2°C	Total Resistance @ 75 °C
-	0.005980	0.005980	0.006020	0.005993	0.020178

WITNESSED BY**TESTED BY****APPROVED BY**



ISO/IEC 17025
NABL NO.T1620

CGL/T1/TTR/ET10335/1A

TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division



Smart solutions.
Strong relationships

Date : 24/06/2015 **W.O.No :** ET10335

Serial No : ET10335/1A

MVA : 30

Customer : ZETDC

MEASUREMENT OF INSULATION RESISTANCE OF WINDING

Top Oil Temp. : 42.60°C Bottom Oil Temp. : 39.80°C Avg. Oil Temp. : 41.2°C

Insulation Resistance in MegaOhms

Measured Between	HV / LV + E	LV / HV + E	HV / LV
Test Voltage[Volts]	5000	5000	5000
After Dielectric Tests			
15 Seconds	8740	5930	8250
60 Seconds	12200	11000	13100
600 Seconds	18900	20200	29300
Absorption Index(60/15)	1.4	1.85	1.59
Polarisation Index(600/60)	1.55	1.84	2.24
Before Dielectric Tests			
15 Seconds	13900	8830	12600
60 Seconds	18600	16000	18700
600 Seconds	27900	35000	45200
Absorption Index(60/15)	1.34	1.81	1.48
Polarisation Index(600/60)	1.5	2.19	2.42

Insulation Resistance in MegaOhms

Terminal No.	Measured Between	Core/Frame	Core/Tank	Frame/Tank
	Test Voltage[Volts]	2500	2500	2500
Before Dielectric Tests				
1	60 Seconds	200	22	2
2	60 Seconds	50	55	5
After Dielectric Tests				
1	60 Seconds	200	2	22

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 03/07/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A**MVA:** 30 **Customer :** ZETDC**MEASUREMENT OF NO LOAD LOSS AND NO LOAD CURRENT****Base MVA for % No-load Current (MVA) : 30****Tap Position No. : 8-8****Transformer Energised from : LV****After Dielectric Tests Date : 03/07/2015**

% kV	Freq. [Hz]	C.T.	R.M.S. Volt (kV)	Current Reading (Amp)				No Load Loss (kW)	No Load Current as % of rated Current	Corr. Losses (kW)
		Ratio	Avg. Volt (kV)	U	V	W	Avg.			
		P.T.		Power Reading (kW)						
		Ratio		W1	W2	W3	Total			
90	50.00	30/1	9.906	1.474	0.941	1.545	1.320	17.160	0.084	17.153
		33000/110	9.902	7.276	4.013	5.867	17.156			
100	50.00	30/1	11.030	2.785	1.856	2.891	2.511	24.110	0.159	24.049
		33000/110	11.002	11.576	5.598	6.931	24.105			
110	50.00	30/1	12.427	23.218	18.501	23.762	21.827	42.060	1.386	40.934
		33000/110	12.103	42.362	10.850	-11.150	42.062			

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFIC**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 25/06/2015 **W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**MEASUREMENT OF LOAD LOSS AND IMPEDANCE VOLTAGE****Combination Name : HV (132 kV)/LV**

Supplied Winding : HV (132 kV)	Shorted Winding : LV	Base MVA : 30
C.T.Ratio : 500/1	P.T.Ratio : 22000/110	
Top Oil Temp : 35.30 °C	Bottom Oil Temp : 32.80 °C	Avg Oil Temp : 34.05 °C

Tap Pos	Rated Parameters		Measured Voltage & Current		% of Rated Curr.	Measured Load Loss			Total Load Loss	Freq
	Volt.	Curr.	Volt.	Curr.		W1	W2	W3		
HV	[kV]	[A]	[V]	[A]		[W]	[W]	[W]	[kW]	[Hz]
1	141.240	122.640	16419.60	125.8900	102.65	46350	43350	37500	127.20	49.98
8	132.000	131.220	14468.90	131.3900	100.13	43950	39600	37050	120.60	50.02
15	122.760	141.100	13247.20	142.1200	100.72	47700	43800	42150	133.65	50.02

Calculations**Supply Side : HV (132 kV)****Short Circuit : LV****Temperature [°C] : 34.05 °C****Measurement****Cooling Type : ONAF [30 MVA]****Combination Name : HV (132 kV)/LV**

Tap Position	1	8	15						
Measured Impedance voltage [Vm]	[V]	16419.60	14468.90	13247.20					
Corrected Impedance Voltage at Rated Current	[V]	15995.71	14450.18	13152.12					
Applied Current [ISc]	A	125.89	131.39	142.12					
Rated Current [IHR]	A	122.64	131.22	141.10					
Measured Load Loss [LLM]	[W]	127200.00	120600.00	133650.00					
Corrected Load Loss At Rated Current [LLC]	[W]	120717.14	120288.12	131738.46					

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 25/06/2015 **W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**MEASUREMENT OF LOAD LOSS AND IMPEDANCE VOLTAGE****Cooling Type :** ONAF [30 MVA]**Combination Name :** HV (132 kV)/LV

Tap Position	1	8	15						
Rated Current [IHR] [HV] A	122.64	131.22	141.10						
Rated Current [ILR] [LV] A	1574.64	1574.64	1574.64						
Avg. Resistance [RhAvg] [HV] at 41.2 °C Ohms	1.106200	1.040467	1.105067						
Avg. Resistance [RIAvg] [LV] at 41.2 °C Ohms	0.0059933	0.0059933	0.0059933						
Copper Loss[I ² R] [CLh] [HV] at 41.2 °C [W]	49913.63	53746.43	66003.03						
Copper Loss[I ² R] [CLI] [LV] at 41.2 °C [W]	44581.00	44581.00	44581.00						
Total Loss[I ² R] at 41.2 °C [W]	94494.63	98327.43	110584.03						
Total Loss[I ² R] [TCL] at 34.05 °C [W]	92031.34	95764.22	107701.32						
Corrected Load Loss [LLC] at 34.05 °C [W]	120717.14	120288.12	131738.46						
Stray Loss [SL =LLC - TCL] at 34.05 °C [W]	28685.80	24523.90	24037.14						
% Z at 34.05 °C %	11.33	10.94	10.71						
% R at 34.05 °C %	402.39	400.96	439.13						
% X at 34.05 °C %	402.23	400.81	439.00						
Total Copper Loss[I ² R] at 75 °C [W]	106058.42	110360.25	124116.76						
Stray Loss at 75 °C [W] At Test Freq	24891.87	21280.42	20858.03						
Stray Loss at 75 °C [W] @ 50 Hz	24911.80	21263.40	20841.36						
Load Loss at 75 °C [W] At Test Freq	130950.29	131640.67	144974.79						
Load Loss at [30 KVA] at 75 °C [W] @ 50 Hz	130970.22	131623.65	144958.12						
% X at 75 °C %	402.23	400.81	439.00						
% R at 75 °C %	436.50	438.80	483.25						
% Z at [30 KVA] at 50 Hz at 75 °C %	593.57	594.30	652.88						

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships

Date : 25/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

MEASUREMENT OF LOAD LOSS AND IMPEDANCE VOLTAGE

Combination Name : HV (88 kV)/LV

Supplied Winding : HV (88 kV)	Shorted Winding : LV	Base MVA : 30
C.T.Ratio : 500/1	P.T.Ratio : 33000/110	
Top Oil Temp : 32.40 °C	Bottom Oil Temp : 30.50 °C	Avg Oil Temp : 31.45 °C

Tap Pos	Rated Parameters		Measured Voltage & Current		% of Rated Curr.	Measured Load Loss			Total Load Loss	Freq
	Volt.	Curr.	Volt.	Curr.		W1	W2	W3		
HV	[kV]	[A]	[V]	[A]		[W]	[W]	[W]	[kW]	[Hz]
1	97.240	178.130	7472.50	138.5900	77.80	23940	22260	19970	66.17	49.96
8	88.000	196.830	7295.80	177.1500	90.00	30860	29940	27350	88.15	49.88
15	78.760	219.920	6064.80	189.5000	86.17	32240	32510	30530	95.28	49.81

Calculations

Supply Side : HV (88 kV) **Short Circuit : LV** **Temperature [°C] : 31.45 °C**

Measurement

Cooling Type : ONAF [30 MVA] Combination Name : HV (88 kV)/LV

Tap Position	1	8	15						
Measured Impedance voltage [Vm]	[V]	7472.50	7295.80	6064.80					
Corrected Impedance Voltage at Rated Current	[V]	9604.42	8106.31	7038.37					
Applied Current [ISc]	A	138.59	177.15	189.50					
Rated Current [IHR]	A	178.13	196.83	219.92					
Measured Load Loss [LLM]	[W]	66170.00	88150.00	95280.00					
Corrected Load Loss At Rated Current [LLC]	[W]	109312.92	108823.47	128325.44					

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships

Date : 25/06/2015 W.O.No : ET10335

Serial No : ET10335/1A

MVA : 30

Customer : ZETDC

MEASUREMENT OF LOAD LOSS AND IMPEDANCE VOLTAGE

Cooling Type : ONAF [30 MVA]

Combination Name : HV (88 kV)/LV

Tap Position	1	8	15						
Rated Current [IHR] [HV] A	178.13	196.83	219.92						
Rated Current [ILR] [LV] A	1574.64	1574.64	1574.64						
Avg. Resistance [RhAvg] [HV] at 41.2 °C Ohms	0.479460	0.416047	0.478307						
Avg. Resistance [RIAvg] [LV] at 41.2 °C Ohms	0.0059933	0.0059933	0.0059933						
Copper Loss[I ² R] [CLh] [HV] at 41.2 °C [W]	45640.22	48355.54	69399.68						
Copper Loss[I ² R] [CLI] [LV] at 41.2 °C [W]	44581.00	44581.00	44581.00						
Total Loss[I ² R] at 41.2 °C [W]	90221.22	92936.54	113980.68						
Total Loss[I ² R] [TCL] at 31.45 °C [W]	87020.03	89639.01	109936.47						
Corrected Load Loss [LLC] at 31.45 °C [W]	109312.92	108823.47	128325.44						
Stray Loss [SL =LLC - TCL] at 31.45 °C [W]	22292.89	19184.46	18388.97						
% Z at 31.45 °C %	9.88	9.23	8.97						
% R at 31.45 °C %	364.38	362.74	427.75						
% X at 31.45 °C %	364.25	362.62	427.66						
Total Copper Loss[I ² R] at 75 °C [W]	101262.05	104309.66	127929.08						
Stray Loss at 75 °C [W] At Test Freq	19157.50	16486.26	15802.65						
Stray Loss at 75 °C [W] @ 50 Hz	19188.19	16565.68	15923.44						
Load Loss at 75 °C [W] At Test Freq	120419.55	120795.92	143731.73						
Load Loss at [30 KVA] at 75 °C [W] @ 50 Hz	120450.24	120875.34	143852.52						
% X at 75 °C %	364.25	362.62	427.66						
% R at 75 °C %	401.40	402.65	479.11						
% Z at [30 KVA] at 50 Hz at 75 °C %	542.03	541.87	642.21						

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFIC

ISO/IEC 17025
NABL NO.T1620

TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

Smart solutions.
Strong relationships

Date : 27/07/2015 **W.O.No :** ET10335

Serial No : ET10335/1A

MVA : 30

Customer : ZETDC

APPLIED VOLTAGE TEST

Winding's Under Test	*Ur[kV]	Test volt [kV]	Test Time(Sec)	Freq.[Hz]	Remarks
HV wdg to other wdg and Tank	132	38	60	50	WITHSTOOD OK
HV wdg to other wdg and Tank	88	38	60	50	WITHSTOOD OK
LV wdg to other wdg and Tank	11	38	60	50	WITHSTOOD OK

***Ur: Rated Line Voltage**

WITNESSED BY

TESTED BY

APPROVED BY

Plot No A-267,MIDC,Road No 16A,Op. ESIS Hospital,Wagle Industrial Estate,Thane(West),400604,India.

Sheet : 15 of 46



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFIC

TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships

Date : 29/07/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

MAGNETIC BALANCE AND EXCITATION CURRENT

For Before Dielectric Tests

Magnetic Balance & Excitation Current for Tap 8 From HV(88 kV) Side.				
Applied Voltage □	1U1 - N [V]	1V1 - N [V]	1W1 - N [V]	Current (mA)
1U1 - N	244.4	220.4	23.2	4.53
1V1 - N	123.5	244.1	120.5	3.15
1W1 - N	18.92	225.2	244.3	4.58

Magnetic Balance & Excitation Current From LV Side.				
Applied Voltage □	2U1 - N [V]	2V1 - N [V]	2W1 - N [V]	Current (mA)
2U1 - N	244.8	188.9	55.4	171.40
2V1 - N	122.8	244.9	121.7	122.50
2W1 - N	55.4	188.8	244.7	170.70

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFIC

TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 29/07/2015 **W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**MAGNETIC BALANCE AND EXCITATION CURRENT****Magnetic Balance & Excitation Current for Tap 8 From HV(132 kV) Side.**

Applied Voltage □	1U1 - N [V]	1V1 - N [V]	1W1 - N [V]	Current (mA)
1U1 - N	234.2	231.7	10.76	2.47
1V1 - N	121.1	234.4	113.1	1.74
1W1 - N	9.68	228.4	234.6	2.38

Magnetic Balance & Excitation Current From LV Side.

Applied Voltage □	2U1 - N [V]	2V1 - N [V]	2W1 - N [V]	Current (mA)
2U1 - N	233.6	184.7	47.4	171.40
2V1 - N	117	232.6	116.5	122.50
2W1 - N	47.8	184	234.2	170.70

WITNESSED BY

TESTED BY

APPROVED BY



ISO/IEC 17025
NABL NO.T1620

CGL/T1/TTR/ET10335/1A

TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

The Automation People
PROLIFIC

Smart solutions.
Strong relationships

Date : 05/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

MEASUREMENT OF POWER TAKEN BY COOLER CIRCUIT

Average voltage L-L	412.5 V
Total Current	4.11 A
Measured Loss	2.91 kW
Guaranteed Loss	3 kW

WITNESSED BY

TESTED BY

APPROVED BY



ISO/IEC 17025
NABL NO.T1620

CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

Smart solutions.
Strong relationships

Date : 24/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

OIL LEAKAGE TEST

- Transformer was subjected to oil leakage test at pressure of 12 PSI measured at bottom of tank. The pressure was sustained for a period of 12 hours and observations were made. No drop in pressure or no leaks observed during the sustained period.

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFIC**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 24/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**MEASUREMENT OF ACOUSTIC NOISE LEVEL****Noise level measured in accordance with specification :****NEMA-TR1****Test Conditions****Excitation voltage[kV]** : 132**Tap position** : 8**Test Frequency[Hz]** : 50**Guaranteed Noise Level [dB]** : 76**Transformer Energised at Rated Voltage**

Point No	Before Energising Transformer Ambient (dB)		Cooling	
	1/3 rd Height	2/3 rd Height	ONAF (dB)	
			1/3 rd Height	2/3 rd Height
1	67.20	67.50	74.30	73.60
2			74.90	73.80
3			74.80	73.90
4	67.10	67.30	75.60	74.40
5			75	76.60
6			75.40	75.70
7	67	67	76	75.80
8			75.40	76.10
9			76.20	74.20
10	67.20	67.20	74.60	73.80
11			73.80	72.70
12			74.20	74
13			73.80	74.20
14	67.30	67.10	76.30	73
15			73.80	73.60
16			73.90	74.20
17			74.80	72.60

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 24/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :**30**Customer :** ZETDC**MEASUREMENT OF ACOUSTIC NOISE LEVEL**

Transformer Energised at Rated Voltage				
Point No	Before Energising Transformer Ambient (dB)		Cooling	
	1/3 rd Height	2/3 rd Height	ONAF (dB)	
			1/3 rd Height	2/3 rd Height
18			74.60	75.40
19	67.40	67.10		
Mean:-	67.20	67.20	74.93	74.46
Mean Avg:-	67.20		74.70	

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 24/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**LIGHTNING IMPULSE VOLTAGE WITHSTAND TEST**

Rated Voltage	Test Voltage [kVp]			Standard Waveform	Polarity
[kV]	FW	-	-	T1/T2/Tc	
132	650	-	-	[1.2 ± 0.36 / 50 ± 10/2-6] μS	[-] Negative
Phase Applied	Phase - 1U1			Phase - 1V1	Phase - 1W1
Terminal	HV(132) - 1U1			HV(132) - 1V1	HV(132) - 1W1
Tap Position	1			8	15
WaveShape	1.17 / 55.74 / NA μs			1.32 / 47.30 / NA μs	1.27 / 47.45 / NA μs

Test Sequence	Wave No.	Voltage		Wave No.	Voltage		Wave No.	Voltage	
		[%]	[kVp]		[%]	[kVp]		[%]	[kVp]
RFW	1	61.60	400.40	1	61.88	402.2	1	61.75	401.4
FW	2	100.00	650	2	100.42	652.7	2	100.12	650.8
FW	3	100.03	650.2	3	100.00	650	3	101.35	658.8
FW	4	100.18	651.2	4	99.97	649.8	4	99.29	645.4

RFW : Reduced Full Wave / FW : Full Wave / RCW : Reduced Chopped Wave / CW : Chopped Wave**Result : Transformer withstood the Test Satisfactory.****WITNESSED BY****TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 24/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**LIGHTNING IMPULSE VOLTAGE WITHSTAND TEST**

Rated Voltage	Test Voltage [kVp]			Standard Waveform	Polarity
[kV]	FW	-	-	T1/T2/Tc	
11	95	-	-	[1.2 ± 0.36 / 50 ± 10/2-6] μS	[-] Negative
Phase Applied	Phase - 2U1			Phase - 2V1	Phase - 2W1
Terminal	LV - 2U1			LV - 2V1	LV - 2W1
Tap Position	-			-	-
WaveShape	1.28 / 42.56 / NA μs			1.28 / 42.93 / NA μs	1.29 / 42.70 / NA μs

Test Sequence	Wave No.	Voltage		Wave No.	Voltage		Wave No.	Voltage	
		[%]	[kVp]		[%]	[kVp]		[%]	[kVp]
RFW	1	53.09	50.44	1	52.11	49.5	1	52.00	49.4
FW	2	100.53	95.5	2	101.37	96.3	2	101.16	96.1
FW	3	100.11	95.1	3	99.79	94.8	3	99.89	94.9
FW	4	99.89	94.9	4	100.00	95.	4	100.11	95.1

RFW : Reduced Full Wave / FW : Full Wave / RCW : Reduced Chopped Wave / CW : Chopped Wave**Result : Transformer withstood the Test Satisfactory.****WITNESSED BY****TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 24/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**LIGHTNING IMPULSE VOLTAGE WITHSTAND TEST**

Rated Voltage	Test Voltage [kVp]			Standard Waveform	Polarity
[kV]	FW	CW	-	T1/T2/Tc	
132	950	950	-	[1.2 ± 0.36 / 50 ± 10/2-6] μS	[-] Negative

Phase Applied	Phase - 1U1	Phase - 1V1	Phase - 1W1
Terminal	HV(132) - 1U1	HV(132) - 1V1	HV(132) - 1W1
Tap Position	1	8	15
WaveShape	1.17 / 55.74 / NA μs	1.32 / 47.30 / NA μs	1.27 / 47.45 / NA μs

Test Sequence	Wave No.	Voltage		Wave No.	Voltage		Wave No.	Voltage	
		[%]	[kVp]		[%]	[kVp]		[%]	[kVp]
RFW	1	42.15	400.40	1	42.34	402.2	1	42.25	401.4
FW	2	68.42	650.0	2	68.71	652.7	2	68.51	650.8
RCW	3	67.53	641.50	3	67.61	642.3	3	67.45	640.8
FCW	4	109.98	1044.8	4	109.92	1044.2	4	109.56	1040.8
FCW	5	109.60	1041.2	5	109.72	1042.3	5	109.65	1041.7
FW	6	68.44	650.2	6	68.42	650.0	6	69.35	658.8
FW	7	68.55	651.2	7	68.40	649.8	7	67.94	645.4

RFW : Reduced Full Wave / FW : Full Wave / RCW : Reduced Chopped Wave / CW : Chopped Wave**Result : Transformer withstood the Test Satisfactory.****WITNESSED BY****TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 24/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**LIGHTNING IMPULSE VOLTAGE WITHSTAND TEST**

Rated Voltage	Test Voltage [kVp]			Standard Waveform	Polarity
[kV]	FW	CW	-	T1/T2/Tc	
11	95	95	-	[1.2 ± 0.36 / 50 ± 10/2-6] μS	[-] Negative
Phase Applied	Phase - 2U1			Phase - 2V1	Phase - 2W1
Terminal	LV - 2U1			LV - 2V1	LV - 2W1
Tap Position	-			-	-
WaveShape	1.28 / 42.56 / NA μs			1.28 / 42.93 / NA μs	1.29 / 42.70 / NA μs

Test Sequence	Wave No.	Voltage		Wave No.	Voltage		Wave No.	Voltage	
		[%]	[kVp]		[%]	[kVp]		[%]	[kVp]
RFW	1	53.09	50.44	1	52.11	49.5	1	52.00	49.4
FW	2	100.53	95.5	2	101.37	96.3	2	101.16	96.1
RCW	3	66.11	62.80	3	64.95	61.7	3	66.42	63.1
FCW	4	107.79	102.4	4	108.53	103.1	4	108.84	103.4
FCW	5	107.16	101.8	5	108.21	102.8	5	108.11	102.7
FW	6	100.11	95.1	6	99.79	94.8	6	99.89	94.9
FW	7	99.89	94.9	7	100.00	95.0	7	100.11	95.1

RFW : Reduced Full Wave / FW : Full Wave / RCW : Reduced Chopped Wave / CW : Chopped Wave**Result : Transformer withstood the Test Satisfactory.****WITNESSED BY****TESTED BY****APPROVED BY**



ISO/IEC 17025
NABL NO.T1620

CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

Smart solutions.
Strong relationships

Date : 26/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

LIGHTNING IMPULSE VOLTAGE WITHSTAND TEST ON NEUTRAL TERMINAL

Winding	HV-N
Test Circuit	Neutral
Impulse On	Neutral (N)
Tap Position	
Wave Shape	μs
Test Voltage	250
Standard Waveform	[1.2 ± 0.36 / 50 ± 10] μS
Polarity	[-] Negative

Test Sequence	Wave No.	Voltage	
		[%]	[kVp]
RFW	1	64.28	160.7
FW	2	99.12	247.8
FW	3	100.36	250.9
FW	4	99.92	249.8

RFW : Reduced Full Wave / FW : Full Wave

Result : Transformer withstood the Test Satisfactory.

WITNESSED BY	TESTED BY	APPROVED BY



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 26/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC**MEASUREMENT OF ZERO PHASE SEQUENCE IMPEDANCE**Cooling Type : **ONAF [30 MVA]** Frequency : **50.01 Hz**Supply : **HV(132)** Short Circuit : - Open : **LV****Supply given between 3-Phase terminals shorted together and Neutral terminal.
Another winding 3-Phase terminals and Neutral Kept open.**

Tap No.	U Rated	I Rated	U Meas.	I Meas.	Ohms	%Z at 50 Hz	Frequency
	[kV]	[Amp]	[kV]	[Amp]	[3V/I]		(Hz)
8	132.0000	131.22	3.061	46.100	199.20	34.294	50.01

Cooling Type : **ONAF [30 MVA]** Frequency : **50.14 Hz**Supply : **HV(132)** Short Circuit : **LV** Open : -**Supply given between 3-Phase terminals shorted together and Neutral terminal.
Another winding 3-Phase terminals and Neutral Shorted.**

Tap No.	U Rated	I Rated	U Meas.	I Meas.	Ohms	%Z at 50 Hz	Frequency
	[kV]	[Amp]	[kV]	[Amp]	[3V/I]		(Hz)
8	132.0000	131.22	0.880	45.200	58.407	10.026	50.14

WITNESSED BY**TESTED BY****APPROVED BY**

Plot No A-267,MIDC,Road No 16A,Op. ESIS Hospital,Wagle Industrial Estate,Thane(West),400604,India.



CGL/T1/TTR/ET10335/1A

ISO/IEC 17025
NABL NO.T1620

TEST CERTIFICATE

Prolific Systems And technology ltd
Transformer (T1) Division

Smart solutions.
Strong relationships

Date : 26/06/2015

W.O.No : ET10335

Serial No : ET10335/1A

MVA : 30

Customer : ZETDC

SWITCHING IMPULSE VOLTAGE WITHSTAND TEST

Rated Voltage	Test Voltage [kVp]			Waveform	Polarity
[kV]	-	-	SI	Tp/Td/Tz	
132	-	-	750	[$\geq 100/\geq 200/\geq 1000$ μ S]	[-] Negative

Phase Applied	Phase - 1U1			Phase - 1V1			Phase - 1W1		
Terminal	HV(132) - 1U1			HV(132) - 1V1			HV(132) - 1W1		
Tap Position	11			11			11		
WaveShape	259.20 / 208.10 / >1000 μ S			255.60 / 204.20 / >1000 μ S			257.10 / 206.80 / >1000 μ S		
Test Sequence	Wave No.	Voltage		Wave No.	Voltage		Wave No.	Voltage	
		[%]	[kVp]		[%]	[kVp]		[%]	[kVp]
RFW	1	66.81	501.1	1	67.76	508.2	1	67.41	505.6
FW	2	100.83	756.2	2	101.09	758.2	2	100.81	756.1
FW	3	100.68	755.1	3	101.35	760.1	3	101.04	757.8
FW	4	100.32	752.4	4	100.55	754.1	4	101.21	759.1

RFW : Reduced Full Wave / FW : Full Wave

Result : Transformer withstood the Test Satisfactory.

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 26/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**MEASUREMENT OF CAPACITANCE AND DISSIPATION FACTOR****For Bushing****Top Oil Temp. : 42.4°C | Bottom Oil Temp. : 39.6°C | Avg. Oil Temp. : 41°C**

Terminal Connected	Make / Sr. No.	Test voltage [kV]	Capacitance [pF]	Tan Delta in % @
				41 °C
HV	HSP/EA20140040 4.1	10.00	255.570	0.366
HV	HSP/EA20140040 5.1	10.00	253.840	0.376
HV	HSP/EA20140040 6.1	10.00	250.260	0.375

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 26/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**MEASUREMENT OF CAPACITANCE AND DISSIPATION FACTOR****For Winding/HV(132)**

Top Oil Temp. : 42.4°C		Bottom Oil Temp. : 39.6°C		Avg. Oil Temp. : 41°C	
Measured Between	Test Voltage [kV]	Capacitance pF	Tan Delta in % @		
			41 °C	20 °C	
HV/LV + E	10.00	7035.840	0.375	0.236	
LV/HV + E	10.00	11593.850	0.567	0.357	
HV/LV + g	10.00	3359.070	0.381	0.240	
LV/HV + g	10.00	7909.200	0.615	0.387	
HV/LV	10.00	3674.470	0.376	0.236	

For Winding/HV(88)

Top Oil Temp. : 42.4°C		Bottom Oil Temp. : 39.6°C		Avg. Oil Temp. : 41°C	
Measured Between	Test Voltage [kV]	Capacitance pF	Tan Delta in % @		
			41 °C	20 °C	
HV/LV + E	10.00	7047.260	0.321	0.202	
LV/HV + E	10.00	11595.810	373.000	234.591	
HV/LV + g	10.00	3361.410	0.322	0.203	
LV/HV + g	10.00	7904.290	0.391	0.246	
HV/LV	10.00	3684.290	0.329	0.207	

tan delta @ 20°C= Tan Delta @ Test Temp./ K, where K =0.6428 X e (0.0222x Avg. Temp.)

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 26/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**INDUCED OVER VOLTAGE WITHSTAND TEST WITH PARTIAL DISCHARGE MEASUREMENT****IVPD****Ur = 132 kV****Calibration Signal :****Test Frequency : 1 Hz****All partial discharge measurements are in pC**

Test Volt. [kV]	Time in Mins		1U1	1V1	1W1
91.450	A	1	50	49	51
120.420	B	5	52	50	53
137.180	C	30 Sec	OK	OK	OK
120.420	D	5	51	52	55
120.420	D	10	53	54	54
120.420	D	15	52	55	54
120.420	D	20	54	55	56
120.420	D	25	53	54	57
120.420	D	30	55	54	56
120.420	D	35	54	55	56
120.420	D	40	532	56	54
120.420	D	45	55	56	54
120.420	D	50	54	57	55
120.420	D	55	55	55	53
120.420	D	60	53	56	52
91.450	E	1	52	51	52

Background PD Level	
Before Test	30.485
After Test	30.485
Guranteed Values	18
Background PD Level	16

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE

Prolific Systems And technology ltd

Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620

Smart solutions.
Strong relationships

Date : 26/06/2015


W.O.No : ET10335

Serial No : ET10335/1A

MVA : 30

Customer : ZETDC

INDUCED OVER VOLTAGE WITHSTAND TEST WITH PARTIAL DISCHARGE MEASUREMENT

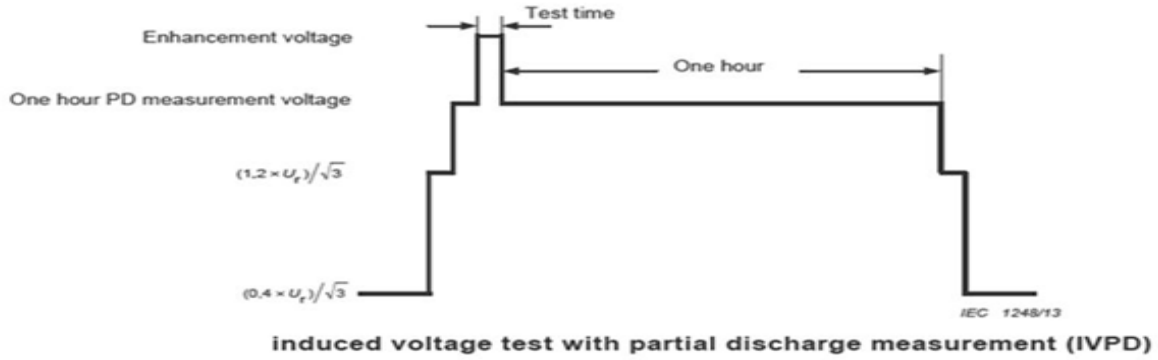

WITNESSED BY

TESTED BY

APPROVED BY



ISO/IEC 17025
NABL NO.T1620

CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

Smart solutions.
Strong relationships

Date : 15/07/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

CHECK OF CT RATIO AND POLARITY

All Bushing CT's Checked for Ratio & Polarity AS PER r & d PLATE DRAWING T0225552VFGHTC

Found to be OK

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships

Date : 26/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

SFRA MEASUREMENT**SFRA for Winding : LV**

TEST OBJECT : 3P2WDualHV
VOLTAGE CLASS : -
W.O. No. : ET10335
SERIAL No. : ET10335/1A
CUSTOMER : ZETDC
TEST DATE : 26/06/2015
TIME OF TEST : Pre - Dispatch
TESTED AT : Transformer (T1) Division

Transformer Condition under Test

- a) Transformer was fully filled with Oil
- b) Transformer tap switch kept at Normal position.
- c) Transformer fitted with bushings.

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A



TEST CERTIFICATE
Prolific Systems And technology ltd
Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships

Date : 26/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A
MVA : 30 **Customer :** ZETDC

SFRA MEASUREMENT**Test Connections**

Trace No	Red Lead position	Black Lead Position	Other Terminal Condition
1	1U1	1N	OPEN
2	1V1	1N	OPEN
3	1W1	1N	OPEN
4	1U1	1N	LV SHORTED
5	1V1	1N	LV SHORTED
6	1W1	1N	LV SHORTED
7	2U1	2N	OPEN
8	2V1	2N	OPEN
9	2W1	2N	OPEN

Test Procedure for Winding : LV

- 1) The transformer tested was completely isolated from the power supply.
- 2) In order to maintain consistency and repeatability of measurements, all terminals that are not under test were isolated and floating.
- 3) SFRA instrument was calibrated as per equipment operating manual.
- 4) Connections of the cables and Ground wire are followed as per the SFRA manual.

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFIC**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 27/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**TEMPERATURE RISE TEST**

Measured no-load loss [kW] [Po]	:	24.246
Load loss [kW] [Pk] [at 75 °C]	:	143.850
Total losses to be fed [kW] [Po + Pk]	:	168.096
Supply side : HV	Short side : LV	Tap position : 15
Rated Current	:	141.097 A
Cooling	:	ONAF [30 MVA]
Yearly Average Ambient Temperature for Hot Spot calculation	:	20 °C

Measurements				TEMPERATURES [°C]										
Hour	kW	kV	A	t1	t2	t3	t4	tAvg	I/L1	O/L1	I/L2	O/L2	ty	dtY
9:30	177.35	7.839	244.16	26.3	26.1	25.9	25.8	26.03	52.3	45.6	52.3	45.7	55.2	29.17
10:30	177.38	7.892	244.32	28.1	28.3	28.7	29.2	28.58	58.3	49.3	58.3	50.3	61.9	33.32
11:30	177.35	7.893	244.16	31.6	31.1	31.5	31.2	31.35	64.3	57.6	64.5	56.8	65.5	34.15
12:30	177.38	7.892	244.32	33.7	34.1	34.4	33.8	34.00	67.2	59.8	67.1	59.5	68.2	34.20
13:30	177.36	7.885	245.17	35.6	36.5	36.2	36.4	36.18	68.9	60.1	68.4	60.3	70.4	34.22
14:30	177.35	7.883	245.43	37.2	37.8	36.9	38.2	37.53	70.3	63.2	69.9	63.8	72.3	34.77
Current reduced to rated current 141.097														
15:30	177.38	7.882	245.22	37.9	38.2	37.1	38.5	37.93	69.8	61.2	69.7	61.5	71.2	33.27
HV(88)/LV Winding ShutDown Phase 1														

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 27/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**TEMPERATURE RISE TEST**


Hour	TEMPERATURES [°C]			
	OTI	WTI-HV	WTI-LV	WTI--
9:30	56	63	64	64
10:30	60	69	70	70
11:30	66	74	74	74
12:30	68	76	78	78
13:30	70	80	78	78
14:30	72	82	80	80
Current reduced to rated current 141.097				
15:30	69.8	61.2	69.7	61.5
HV(88)/LV Winding ShutDown Phase 1				

t1.... t3/t4 : Ambient Temperature	I/L1...I/L2 : Cooler Inlet Temp.	ty : Top Oil Temperature
tAvg : Avg. Ambient Temp.	O/L1..O/L2 : Cooler Outlet Temp.	dty : Top Oil Temp. Rise
FO : Fibre Optics	OTI : Oil Temp. Indicator	WTI :Winding Temp. Indicator
W/I1...W/I2 : Water Inlet Temp.	W/O1...W/O2 : Water Outlet Temp.	CB : Cable Box
MB : Marshalling Box		

WITNESSED BY**TESTED BY****APPROVED BY**

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 27/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**TEMPERATURE RISE TEST****RESISTANCE - TIME CURVE**

Time [Sec]	HV(88) R[Ω]	Ext.Pol. R[Ω]
0		0.563527
30		0.563068
60		0.562623
90		0.562191
120		0.561774
150	0.5613639	0.561370
180	0.5609943	0.560980
210	0.5605963	0.560603
240	0.5602268	0.560240
270	0.5598856	0.559891
300	0.5595729	0.559556
330	0.5592886	0.559234
360	0.5588622	0.558926
390	0.5586348	0.558632
420	0.5583505	0.558352
450	0.5580947	0.558085
480	0.5578104	0.557832

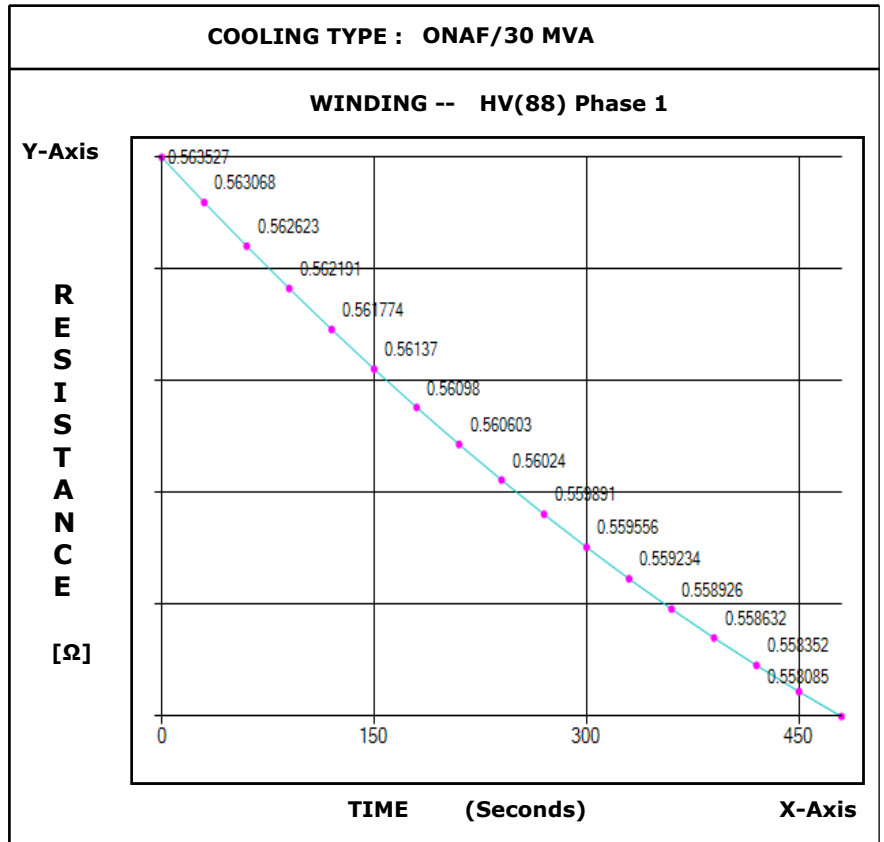**WITNESSED BY****TESTED BY****APPROVED BY**



TEST CERTIFICATE

Prolific Systems And technology ltd

Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620

Smart solutions.
Strong relationships


Date : 27/06/2015 **W.O.No :** ET10335 **Serial No :** ET10335/1A

MVA : 30 **Customer :** ZETDC

TEMPERATURE RISE TEST

RESISTANCE - TIME CURVE

Time [Sec]	LV R[Ω]	Ext.Pol. R[Ω]
0		0.006820
30		0.006793
60		0.006767
90		0.006744
120		0.006723
150	0.0067087	0.006703
180	0.0066844	0.006686
210	0.0066658	0.006670
240	0.0066509	0.006656
270	0.0066398	0.006643
300	0.0066353	0.006633
330	0.0066285	0.006625
360	0.0066212	0.006618
390	0.0066162	0.006613
420	0.0066104	0.006610
450	0.0066051	0.006609
480	0.0066016	0.006610

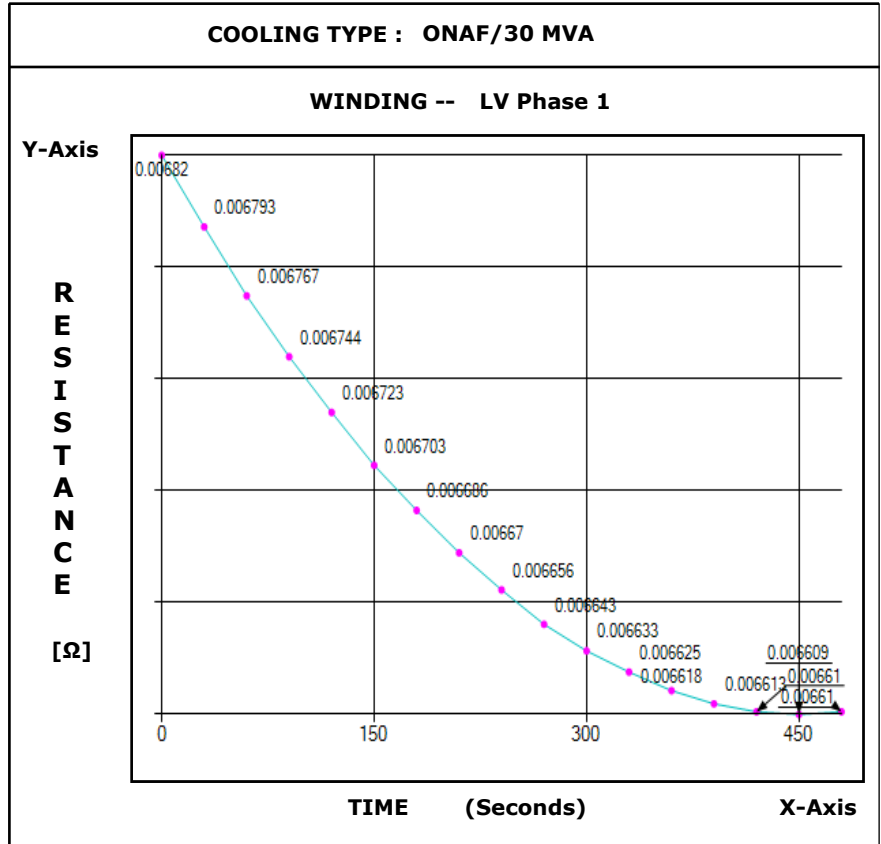

WITNESSED BY

TESTED BY

APPROVED BY



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 27/06/2015 **W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**TEMPERATURE RISE TEST**

DETERMINATION OF TOP OIL TEMP. RISE		HV(88)	LV
Reference Power	MVA	ONAF/30	ONAF/30
Total Losses Supplied	kW	177.35	177.35
Input Rated Losses to be fed	kW	168.096	168.096
Top Oil Temp. Rise at Supplied Losses	°C	34.77	34.77
Corrected Top Oil Temp. Rise to the Input Rated Loss	°C	34.77	34.77
Cooler Inlet Temp. [1st group]	°C	70.3	70.3
Cooler Inlet Temp. [2nd group]	°C	69.9	69.9
Average [Cooler Inlet Temp.]	°C	70.1	70.1
Cooler Outlet Temp.[1st group]	°C	63.2	63.2
Cooler Outlet Temp.[2nd group]	°C	63.8	63.8
Average [Cooler Outlet Temp.]	°C	63.5	63.5
Average Oil Rise at Steady State	°C	31.47	31.47
DETERMINATION OF WINDING TEMP. RISE		HV(88)	LV
Reference Power	MVA	ONAF/30	ONAF/30
Top Oil Temp. Rise @ Rated Current	°C	33.27	33.27
Cooler Inlet Temp. [1nd group]	°C	69.8	69.8
Cooler Inlet Temp. [2nd group]	°C	69.7	69.7
Average [Cooler Inlet Temp.]	°C	69.75	69.75
Cooler Outlet Temp. [1st group]	°C	61.2	61.2
Cooler Outlet Temp. [2nd group]	°C	61.5	61.5
Average [Cooler Outlet Temp.]	°C	61.35	61.35
Avg. Oil Rise at Shutdown	°C	29.07	29.07
Reference Cold Resistance at :41.2°C	Ohms	0.47756	0.00598
Winding Resis. at Shutdown From (Cooling Curve)	Ohms	0.563527	0.00682
Winding Temp. at Shutdown	°C	90.92	80.00
Average Ambient Temp. at Shutdown	°C	37.93	37.93
Gradiant	°C	23.92	13.00
Hot Spot Temp.	°C	85.87	71.67
RESULTS		HV(88)	LV
Top Oil Temp. Rise	°C	34.77	34.77
Winding Temp. Rise	°C	55.39	44.47
Hot Spot Temp.Rise	°C	65.866	51.67
GUAR. VALUE	Top Oil Temperature Rise	°C	60
	Mean Winding Temp. Rise	°C	65
	Hot spot tempeature Rise	°C	20

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 27/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**TEMPERATURE RISE TEST**

Measured no-load loss [kW] [Po]	:	24.246
Load loss [kW] [Pk] [at 75 °C]	:	63.933
Total losses to be fed [kW] [Po + Pk]	:	88.179
Supply side : HV Short side : LV Tap position :		15
Rated Current	:	94.064 A
Cooling	:	ONAN [20 MVA]
Yearly Average Ambient Temperature for Hot Spot calculation	:	20 °C

Measurements				TEMPERATURES [°C]										
Hour	kW	kV	A	t1	t2	t3	t4	tAvg	I/L1	O/L1	I/L2	O/L2	ty	dty
1:00	94.53	5.760	178.84	25.8	26.2	26.3	26.2	26.13	41.0	28.3	41.1	28.9	41.3	15.17
2:00	94.52	5.772	178.86	24.7	24.7	24.5	24.3	24.55	49.5	35.3	49.8	35.7	50.2	25.65
3:00	94.53	5.759	178.88	24.5	24.3	24.2	24.1	24.28	51.3	39.5	51.2	39.1	52.5	28.22
4:00	94.55	5.762	178.85	23.8	24.2	23.7	24.1	23.95	52.2	41.2	52.5	41.4	53.1	29.15
5:00	94.52	5.761	178.89	23.5	23.9	23.5	24.0	23.73	52.6	43.5	52.9	43.7	53.5	29.77
6:00	94.56	5.762	178.91	23.1	23.5	23.2	23.7	23.38	52.9	44.2	53.5	44.3	53.8	30.42
7:00	94.53	5.763	178.88	22.8	23.1	22.9	23.3	23.03	53.2	45.0	53.8	45.1	54.2	31.17
Current reduced to rated current 94.064														
8:00	94.53	5.763	178.88	23.5	23.9	23.8	23.9	23.78	52.0	44.5	52.4	44.6	53.2	29.42
HV(88)/LV Winding ShutDown Phase 2														

WITNESSED BY**TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 27/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**TEMPERATURE RISE TEST**

Hour	TEMPERATURES [°C]			
	OTI	WTI-HV	WTI-LV	WTI--
1:00	39.00	48.00	48.00	50.00
2:00	48.00	56.00	56.00	56.00
3:00	50.00	60.00	60.00	58.00
4:00	52.00	60.00	60.00	60.00
5:00	52.00	60.00	60.00	60.00
6:00	52.00	62.00	62.00	62.00
7:00	54.00	62.00	62.00	62.00
Current reduced to rated current 94.064				
8:00	50.00	58.00	58.00	58.00
HV(88)/LV Winding ShutDown Phase 2				

t1..... t3/t4 : Ambient Temperature	I/L1....I/L2 : Cooler Inlet Temp.	ty : Top Oil Temperature
tAvg : Avg. Ambient Temp.	O/L1..O/L2 : Cooler Outlet Temp.	dty : Top Oil Temp. Rise
FO : Fibre Optics	OTI : Oil Temp. Indicator	WTI :Winding Temp. Indicator
W/I1...W/I2 : Water Inlet Temp.	W/O1...W/O2 : Water Outlet Temp.	CB : Cable Box
MB : Marshalling Box		

WITNESSED BY**TESTED BY****APPROVED BY**

**TEST CERTIFICATE**

Prolific Systems And technology ltd

Transformer (T1) Division

ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships

Date : 27/06/2015

W.O.No : ET10335

Serial No : ET10335/1A

MVA : 30


Customer : ZETDC

TEMPERATURE RISE TEST**RESISTANCE - TIME CURVE**

Time [Sec]	HV(88) R[Ω]	Ext.Pol. R[Ω]
0		0.525346
30		0.524923
60		0.524511
90		0.524113
120		0.523726
150	0.523343	0.523352
180	0.523012	0.522991
210	0.522625	0.522642
240	0.522293	0.522305
270	0.521989	0.521981
300	0.521686	0.521669
330	0.521409	0.521369
360	0.521023	0.521082
390	0.520802	0.520808
420	0.520553	0.520546
450	0.520304	0.520296
480	0.520028	0.520059

COOLING TYPE : ONAN/20 MVA

WINDING -- HV(88) Phase 2

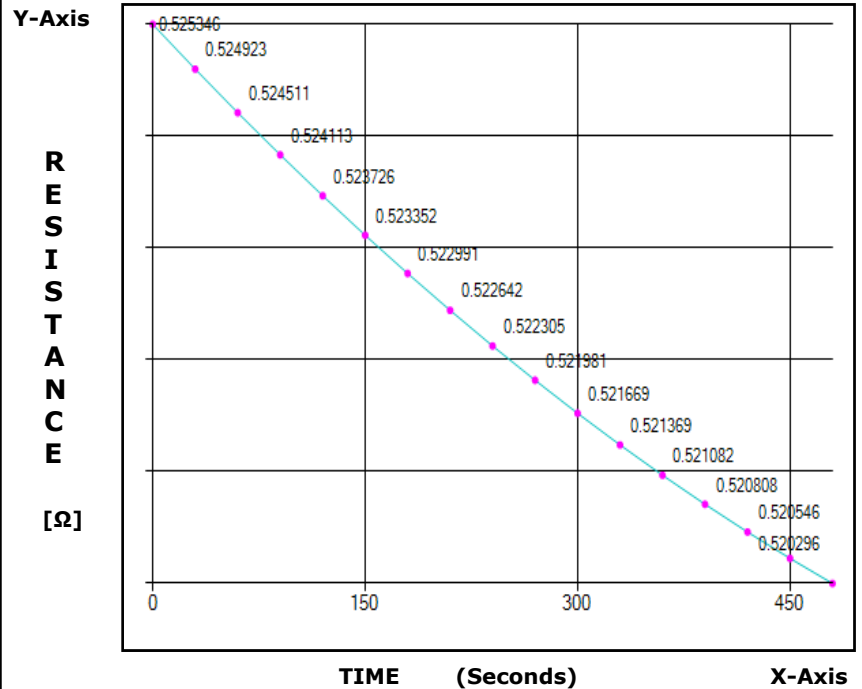


WITNESSED BY

TESTED BY

APPROVED BY

**TEST CERTIFICATE****Prolific Systems And technology ltd****Transformer (T1) Division**ISO/IEC 17025
NABL NO.T1620Smart solutions.
Strong relationships**Date :** 27/06/2015**W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**TEMPERATURE RISE TEST****RESISTANCE - TIME CURVE**

Time [Sec]	LV R[Ω]	Ext.Pol. R[Ω]
0		0.006332
30		0.006294
60		0.006260
90		0.006228
120		0.006199
150	0.006178	0.006173
180	0.006161	0.006150
210	0.006115	0.006130
240	0.006102	0.006112
270	0.006094	0.006098
300	0.006090	0.006086
330	0.006083	0.006077
360	0.006077	0.006071
390	0.006072	0.006067
420	0.006067	0.006067
450	0.006062	0.006069
480	0.006057	0.006074

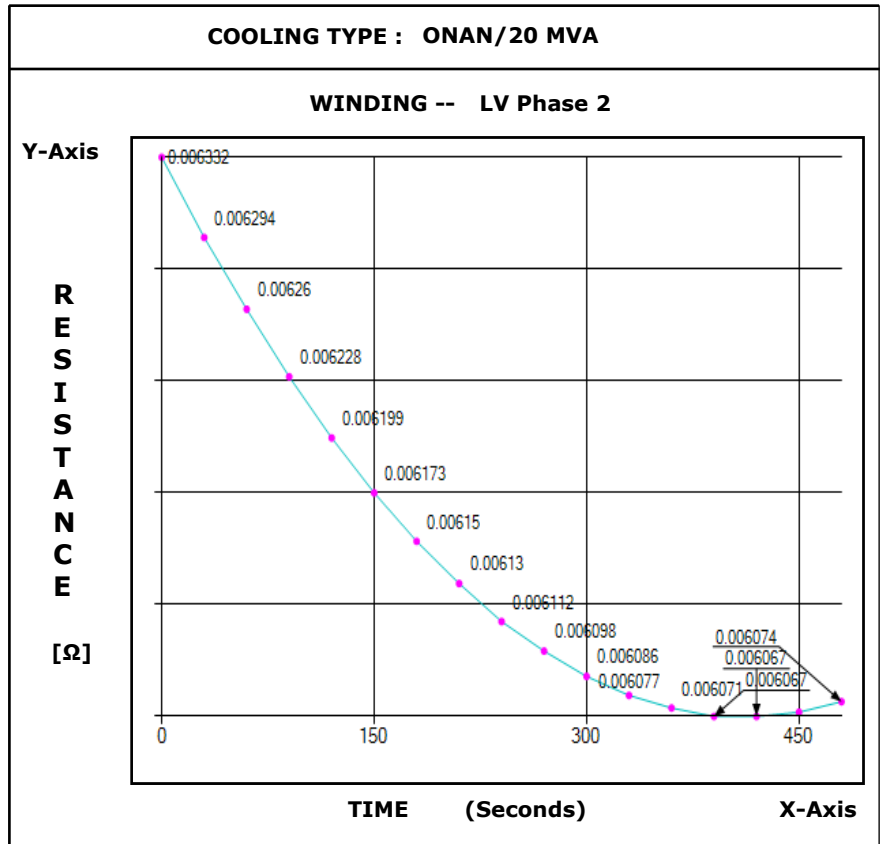**WITNESSED BY****TESTED BY****APPROVED BY**



CGL/T1/TTR/ET10335/1A

The Automation People
PROLIFICISO/IEC 17025
NABL NO.T1620**TEST CERTIFICATE**
Prolific Systems And technology ltd
Transformer (T1) DivisionSmart solutions.
Strong relationships**Date :** 27/06/2015 **W.O.No :** ET10335**Serial No :** ET10335/1A**MVA :** 30**Customer :** ZETDC**TEMPERATURE RISE TEST**

DETERMINATION OF TOP OIL TEMP. RISE		HV(88)	LV
Reference Power	MVA	ONAN/20	ONAN/20
Total Losses Supplied	kW	94.53	94.53
Input Rated Losses to be fed	kW	88.179	88.179
Top Oil Temp. Rise at Supplied Losses	°C	31.17	31.17
Corrected Top Oil Temp. Rise to the Input Rated Loss	°C	31.17	31.17
Cooler Inlet Temp. [1st group]	°C	53.2	53.2
Cooler Inlet Temp. [2nd group]	°C	53.8	53.8
Average [Cooler Inlet Temp.]	°C	53.5	53.5
Cooler Outlet Temp.[1st group]	°C	45.0	45.0
Cooler Outlet Temp.[2nd group]	°C	45.1	45.1
Average [Cooler Outlet Temp.]	°C	45.05	45.05
Average Oil Rise at Steady State	°C	26.95	26.95
DETERMINATION OF WINDING TEMP. RISE		HV(88)	LV
Reference Power	MVA	ONAN/20	ONAN/20
Top Oil Temp. Rise @ Rated Current	°C	29.42	29.42
Cooler Inlet Temp. [1nd group]	°C	52.0	52.0
Cooler Inlet Temp. [2nd group]	°C	52.4	52.4
Average [Cooler Inlet Temp.]	°C	52.2	52.2
Cooler Outlet Temp. [1st group]	°C	44.5	44.5
Cooler Outlet Temp. [2nd group]	°C	44.6	44.6
Average [Cooler Outlet Temp.]	°C	44.55	44.55
Avg. Oil Rise at Shutdown	°C	25.60	25.60
Reference Cold Resistance at :41.2°C	Ohms	0.47838	0.00598
Winding Resis. at Shutdown From (Cooling Curve)	Ohms	0.525346	0.006332
Winding Temp. at Shutdown	°C	68.32	57.46
Average Ambient Temp. at Shutdown	°C	23.78	23.78
Gradiant	°C	18.94	8.08
Hot Spot Temp.	°C	75.79	61.67
RESULTS		HV(88)	LV
Top Oil Temp. Rise	°C	31.17	31.17
Winding Temp. Rise	°C	45.89	35.03
Hot Spot Temp.Rise	°C	55.792	41.674
GUAR. VALUE	Top Oil Temperature Rise	°C	60
	Mean Winding Temp. Rise	°C	65
	Hot spot tempeature Rise	°C	20

WITNESSED BY**TESTED BY****APPROVED BY**
